Site 14

Client Name:

Roland

Client Address:

1010 Suncrest Street, Bryan, 77803

Phone Number:

979-599-0073

Distance from the Church:

2.4 miles - 8 minutes

Description of the work:

Demo existing porch

Rebuild porch

Other Notes:

There is a metal roof that will determine the exact size of the deck

Look into adding gutter that is on site to roof

Little shade

Might be 4 blocks on site to reuse

Site 14

Site Pictures






Site 14

Rendered Project

“Build to site not to plan”



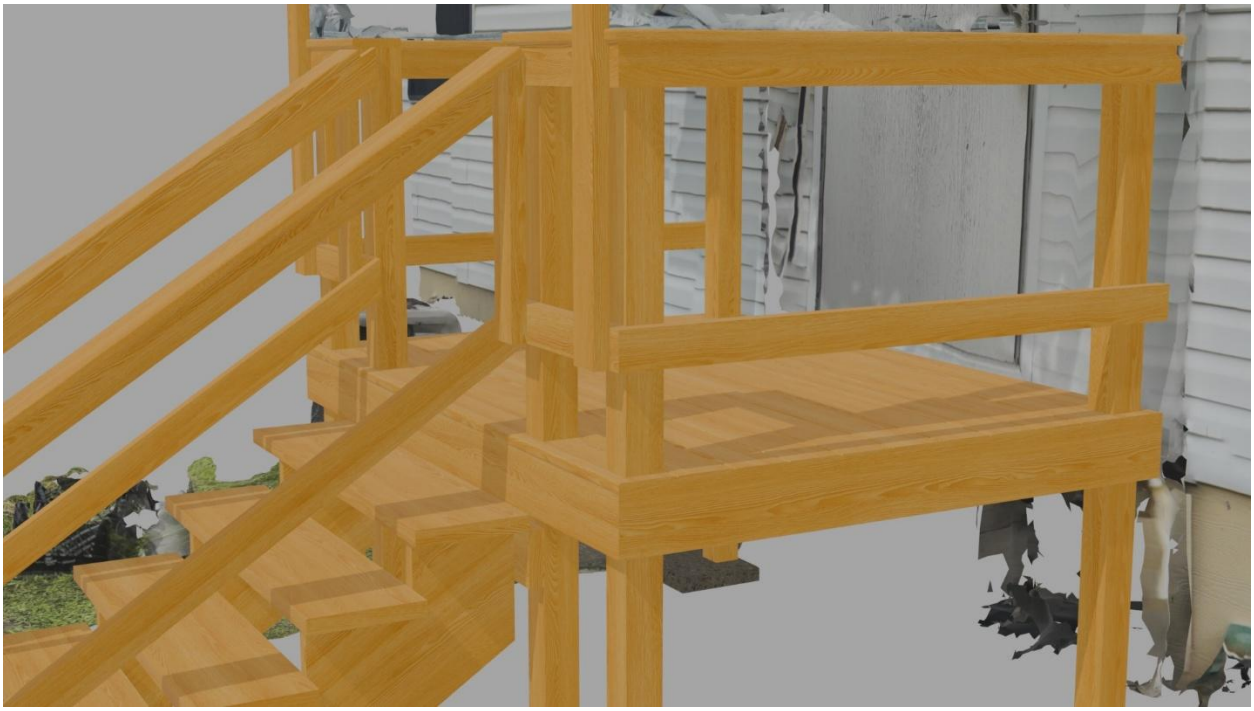

Site 14

Building Notes

- Frame
  - Width and length should match the roof
  - Add extra 4ft 2x4 to better support the roof in the front
- Handrails and posts
  - Check with clients with how they would like the stairs, design shown is in the middle
    - If client wants the stairs to either side of the deck you can save a post
- Decking
  - Might want to start with the complex first cut with the 4 posts
    - Support any part of the deck with cleats if needed
- Stairs
  - Do NOT trust the design
  - Remeasure and recalculate on site
