Site 7

Client Name:

Sheronda Baisy

Client Address:

441 Silkwood Drive, Bryan, 77803

Phone Number:

979-213-8125

Distance from the Church:

2.7 miles - 8 minutes

Description of the work:

Demo existing broken deck

Replace with larger 8x16 deck

Other Notes:

There is a set of concrete stairs that we will reuse


Look into patching small hole in wall from tree falling

Potential shade under car canopy

Very talkative child

Site 7

Site Pictures

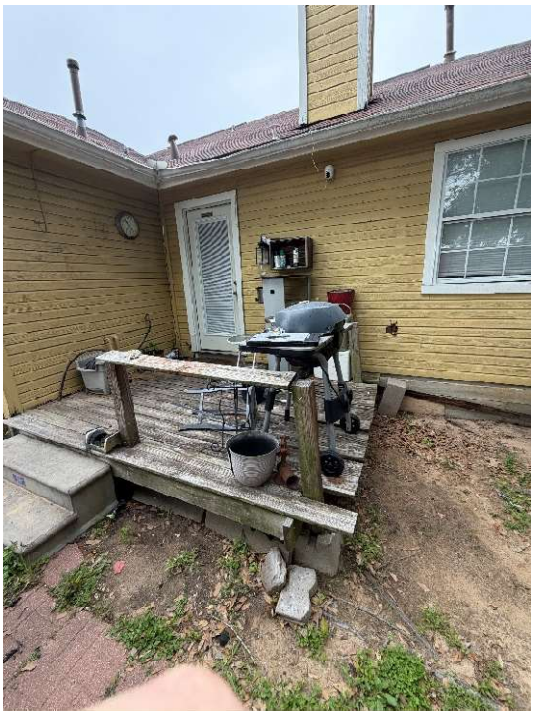





Site 7

Rendered Project

“Build to site not to plan”





Site 7

Building Notes

- Frame
  - Focus on the “Top-left” closest corner to the house
  - See if paver or deck block will be used
  - Check with the client if they want a full 8ft or to the end of the house
  - Don’t forget to cleat the back
- Joists
  - Middle posts interfere with perfect joist spacing
  - Move either the back post or joist
- Handrails
  - Watch lumber used
- Decking
  - You will have to cut out a post and rip one board
- Special Handrail
  - Attach a 2x4 to the bottom of the 4x4 before mounting to frame
  - Use the pavers to create a level surface for the stairs and handrail
  - Add extra support as needed
  - Could also be opted to build a normal handrail
