Site 16

Client Name:

Shelia Goosby

Client Address:

213 Plum Street, Bryan, 77803

Phone Number:

979-092-1012

Distance from the Church:

1.2 miles - 4 minutes

Description of the work:

Demo 2 deck and rebuild

Demo ramp and rebuild

Other Notes:

Little shade

Site 16

Site Pictures





Site 16






Site 16

Rendered Project - “A” Ramp



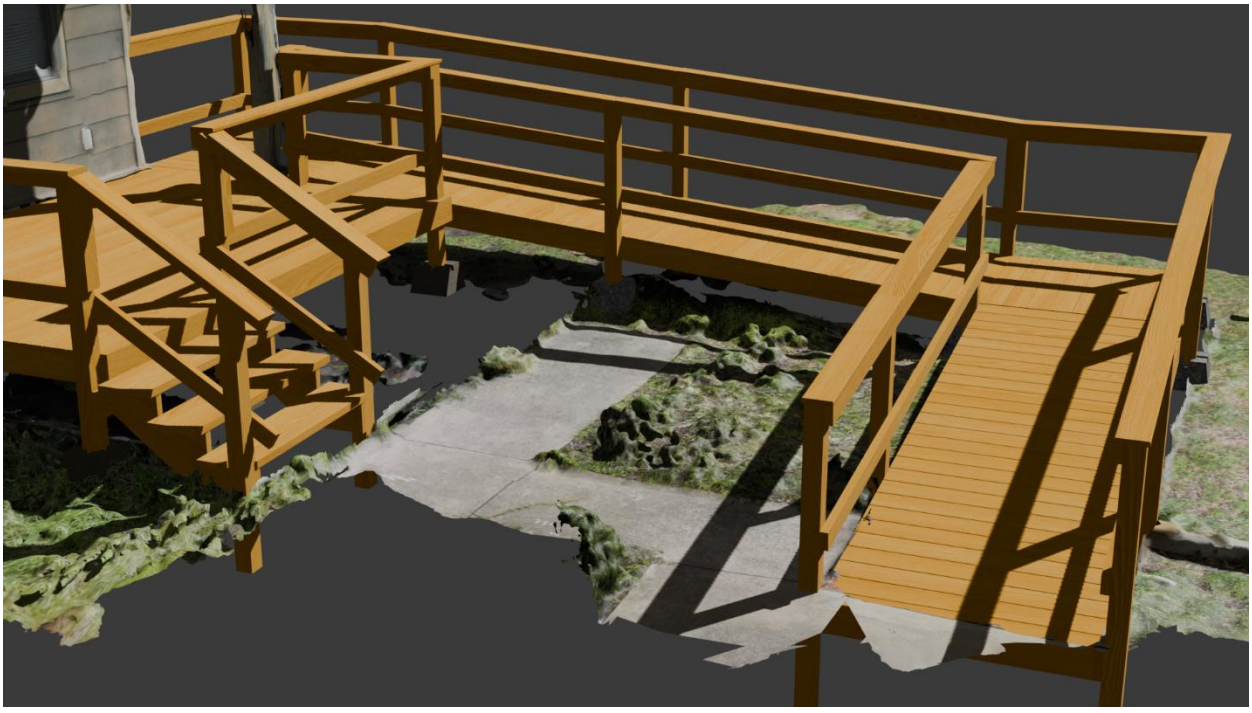

Site 16

Rendered Project - “B” Front deck





Site 16

Rendered Project - “C” Back deck








Site 16

Building Notes


- Project A Ramp
  - The deck transition to the ramp is the hardest part
    - Keep in mind the gutter
    - The deck can be any width, minimum is 55 inches
- Project B Deck
  - The first priority of this project is to determine whether a 2x4 frame with deck boards, or to redeck and build a threshold ramp
    - You are given no extra lumber and should be the first thing
  - Your extra 2x12 box is redecked with deck boards and make sure they line up if the house deck is redecked with 2x6s
  - Since the width of the box is 4ft, I do not have it using joist hangers
- Project C Deck
  - Make sure the deck is next to the house
  - The longer 12ft 2x12 should be used on this house

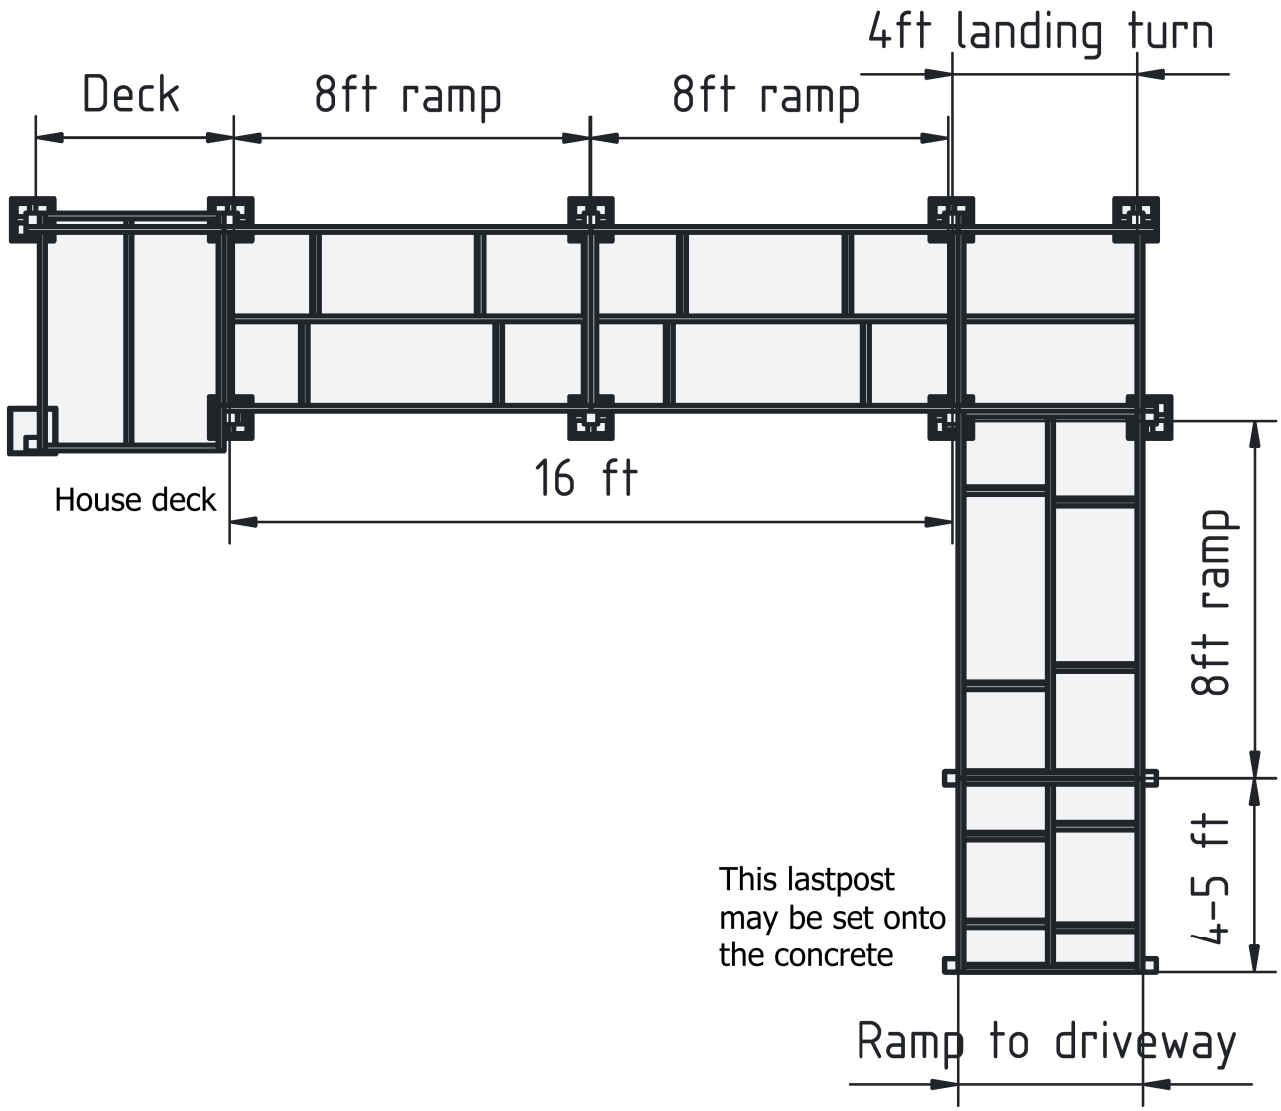
4ft landing turn
Deck
8ft ramp
8ft ramp
House deck
16 ft
8ft ramp
4-5 ft
This lastpost
may be set onto
the concrete
Ramp to driveway

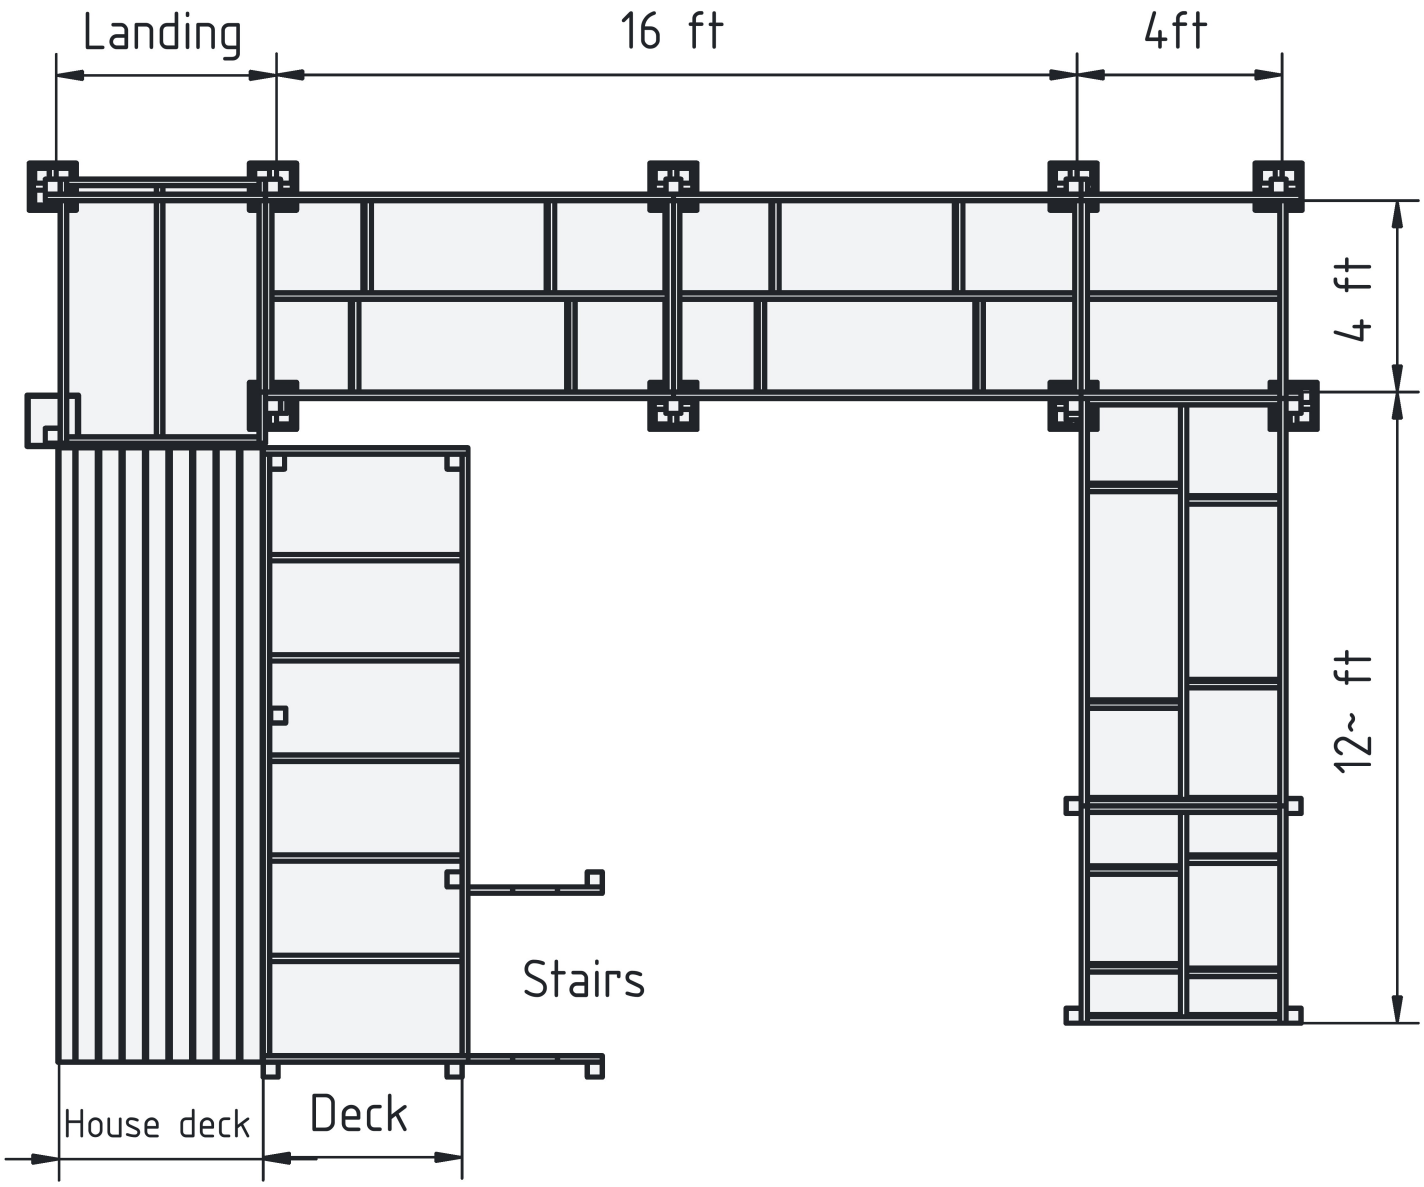

Landing
16 ft
4ft
4 ft
12~ ft
Stairs
House deck
Deck

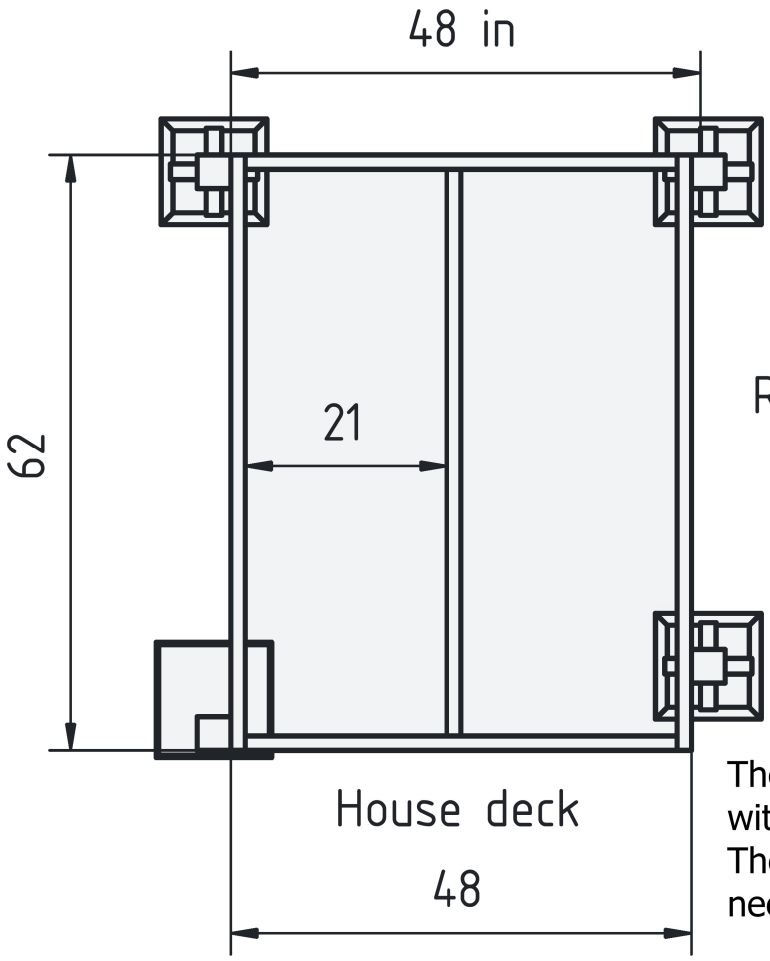

There is the house post
with a gutter on this corner
The handrail and box may
need to be adjusted to accommodate

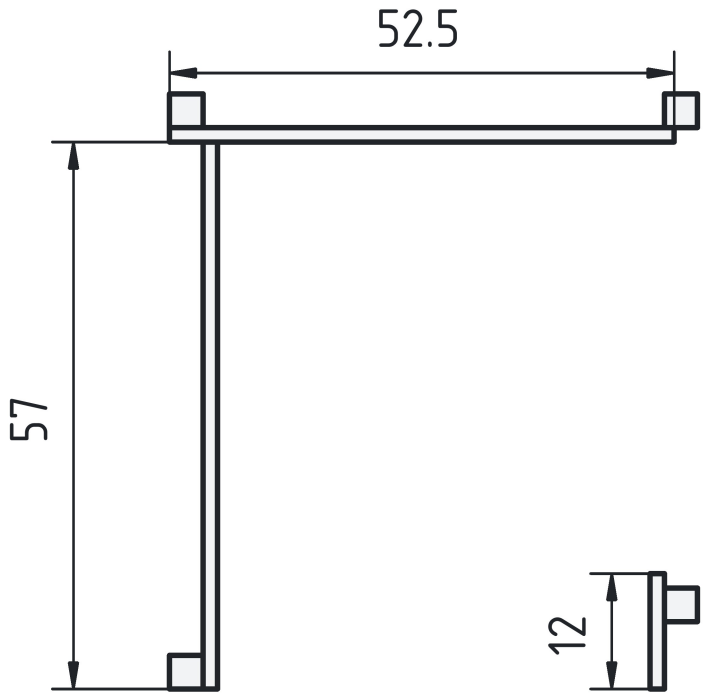



Handrail and posts

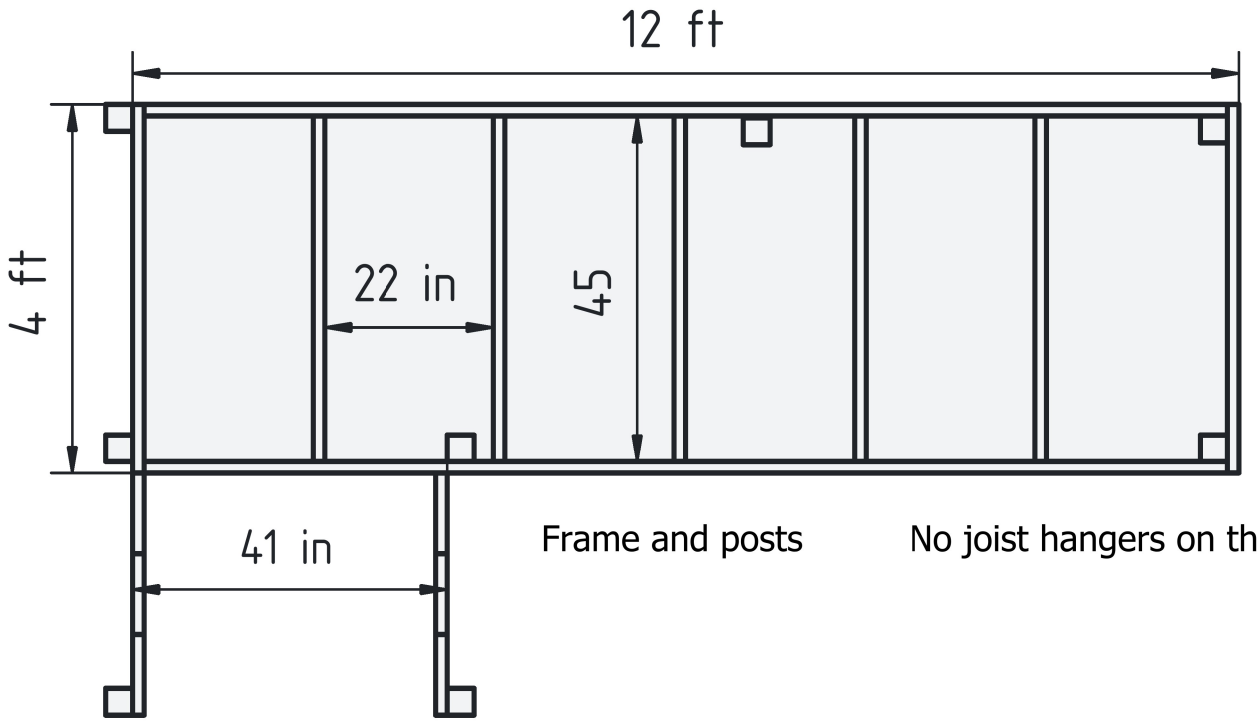


Frame and posts

No joist hangers on this deck

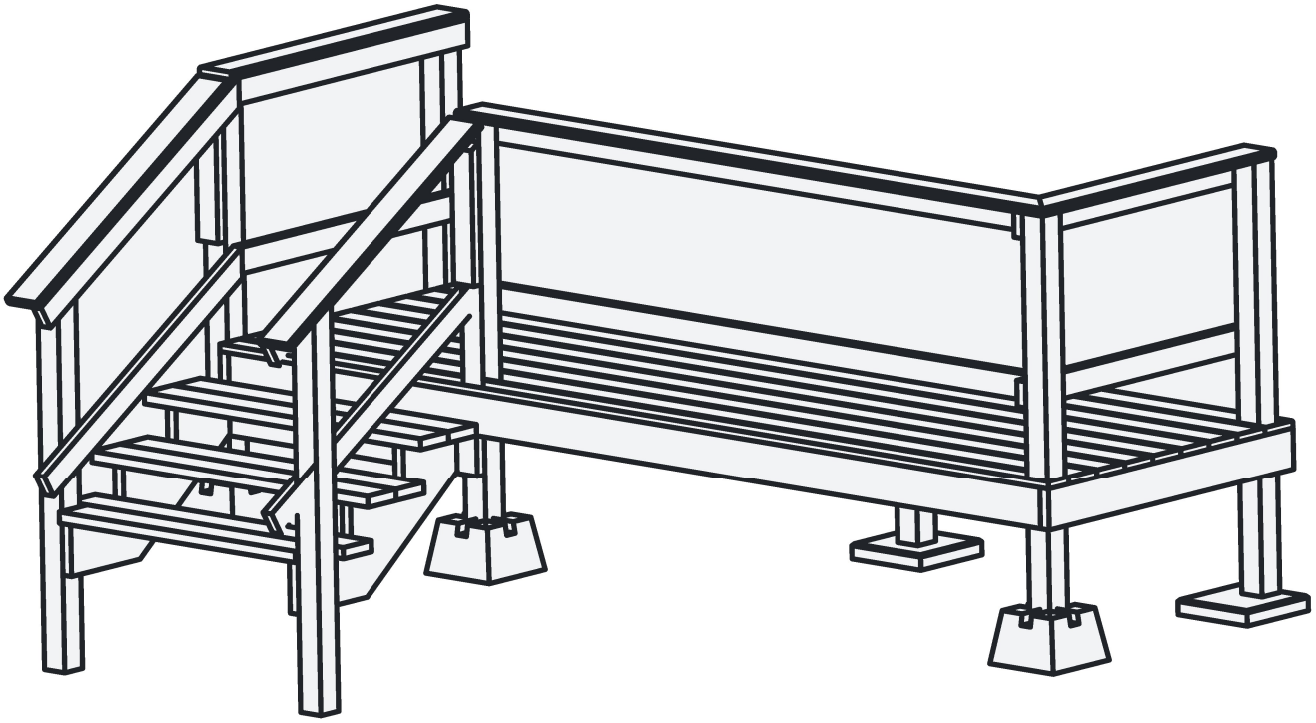

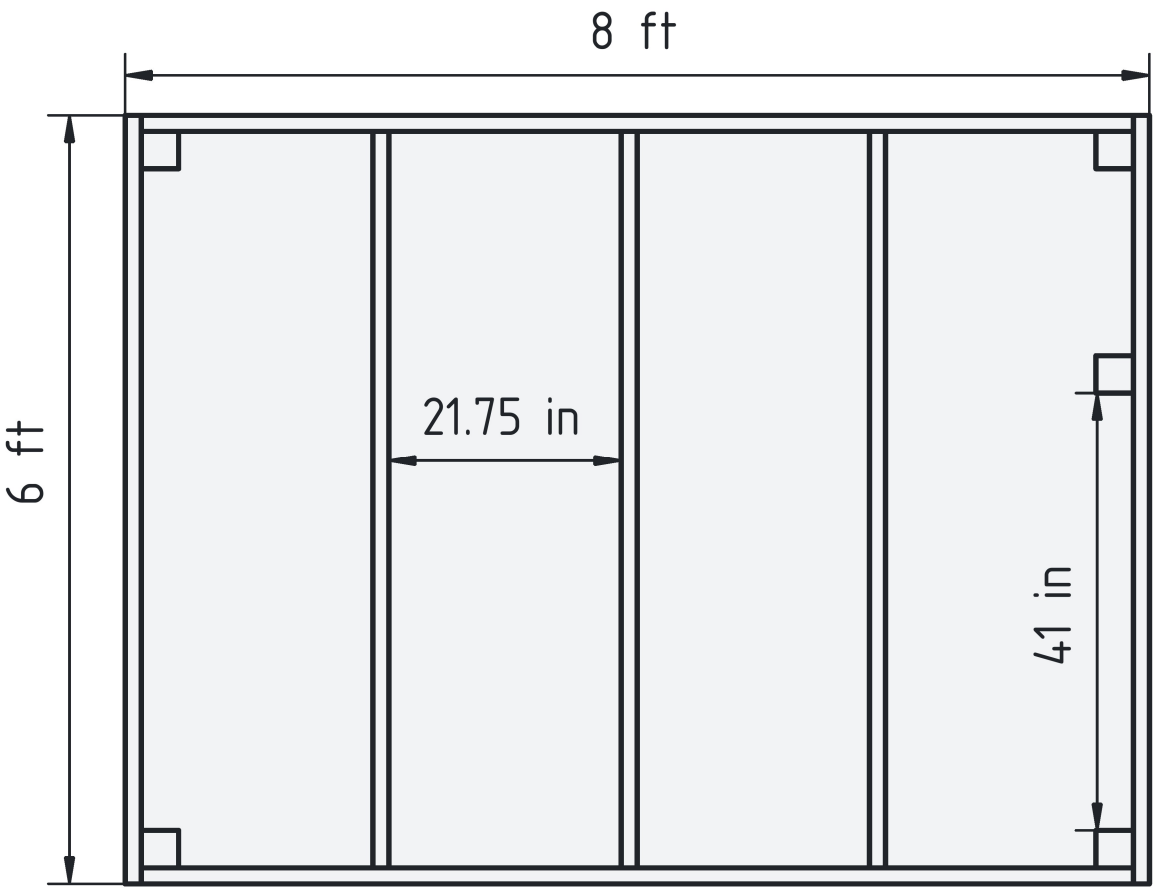
8 ft
6 ft
21.75 in
41 in

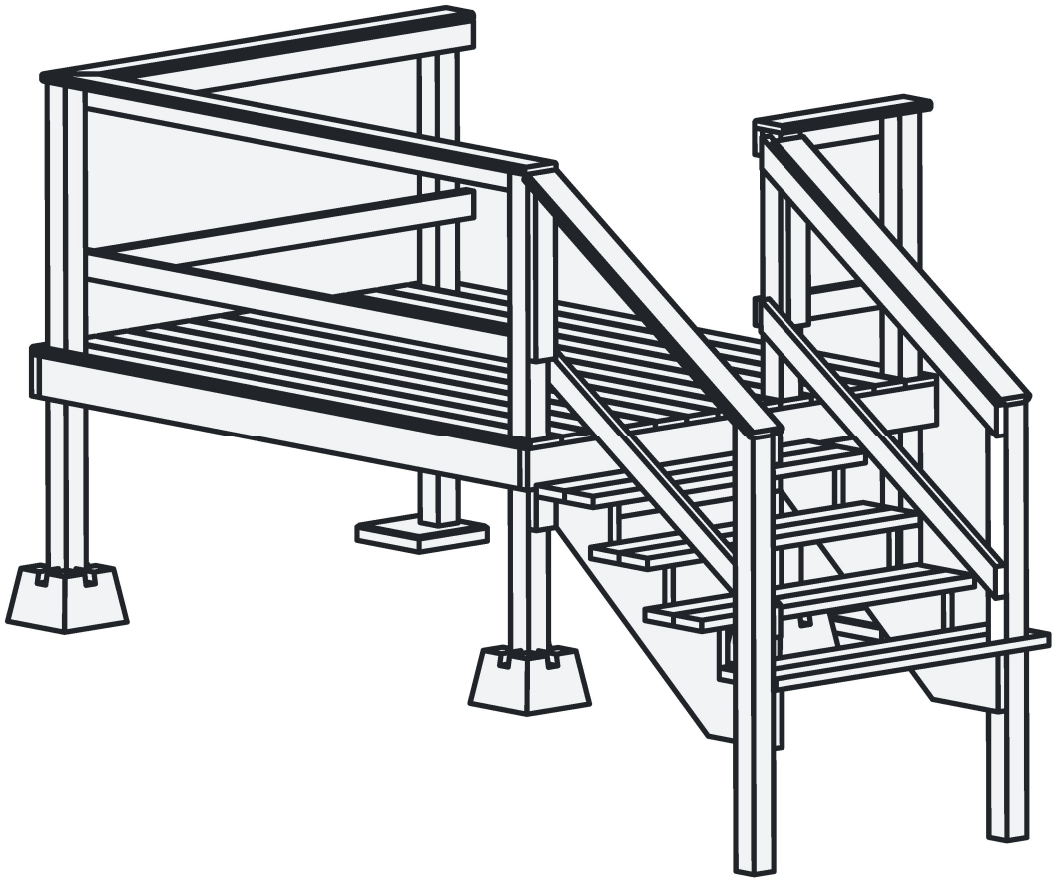

Materials List

Part A

Item	Amount
Frames	
2x6x8	31
Handrails	
2x4x8	25
Deckboard 8ft	13
All Decking	
Deckboard 8ft	42
Posts	
Pavers	5
Deck Block	10
4x4x8	14
Concrete Bag	2
Cleats	
2x6x8	1
2x4x8	1

Part B

Item	Amount
Frame	
2x6x8	4
2x6x12	2
4x4x8	6
Pavers	3
Deck Block	3
Handrails	
2x4x8	4
2x4x12	2
Deckboard 8ft	2
Deckboard 12ft	1
Decking	
Deckboard 12ft	9
Stairs	
4x4x8	2
Concrete Bag	1
2x12x10	1
2x6x8	4
2x4x8	4
Deckboard 8ft	2
Stringer strap	2

Materials List

Part C

Item	Amount
Frame	
2x6x8	7
4x4x8	5
Pavers	2
Joist Hangers	6
Deck Block	3
Handrails	
2x4x8	5
Deckboard 8ft	3
Decking	
Deckboard 8ft	13
Stairs	
4x4x8	2
Concrete Bag	1
2x12x12	1
2x6x8	5
2x4x8	4
Deckboard 8ft	2
Stringer strap	2

Total	
2x6x8	52
4x4x8	29
2x4x8	43
2x6x12	2
2x4x12	2
2x12x10	1
2x12x12	1
Deckboard 8ft	77
Deckboard 12ft	19
Deck Block	16
Pavers	10
Concrete Bag	4
Stringer strap	4
Joist Hangers	6
