Site 14

Client Name:

Roland

Client Address:

1010 Suncrest Street, Bryan, 77803

Phone Number:

979-599-0073

Distance from the Church:

2.4 miles - 8 minutes

Description of the work:

Demo existing porch

Rebuild porch

Other Notes:

There is a metal roof that will determine the exact size of the deck

Look into adding gutter that is on site to roof

Little shade

Site 14

Site Pictures






Site 14

Rendered Project

“Build to site not to plan”




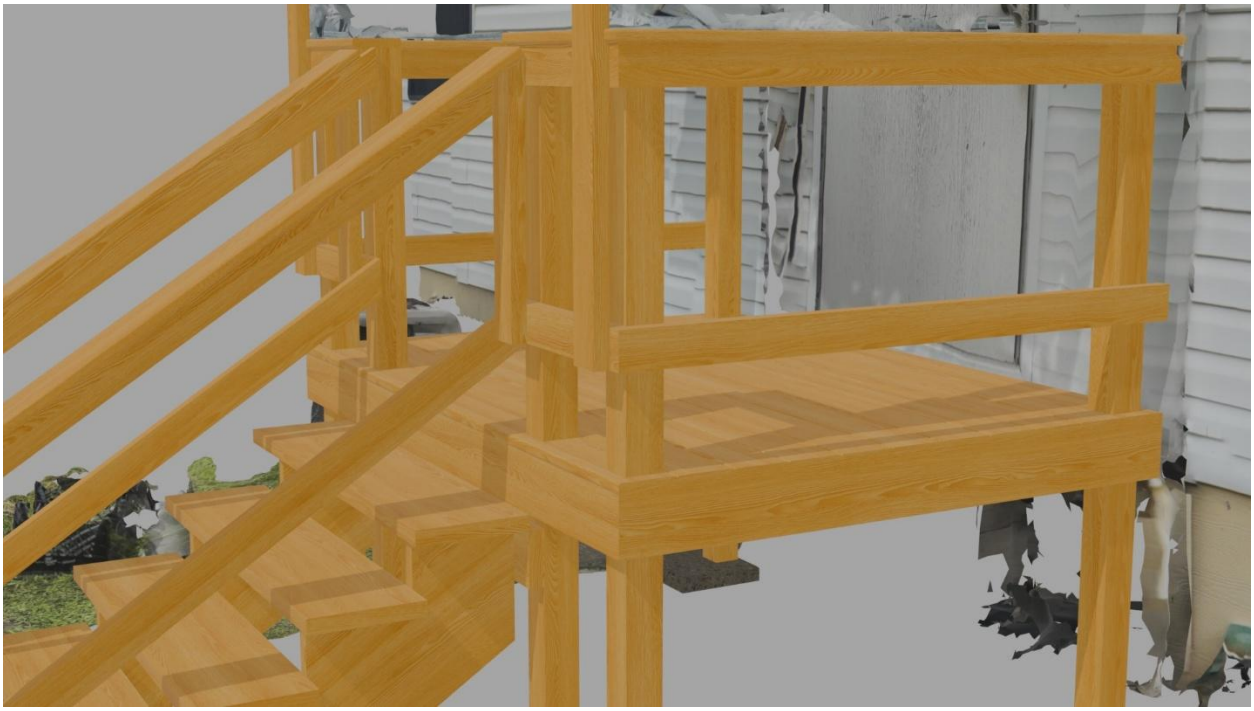


Site 14

Building Notes


- Frame
  - Width and length should match the roof
  - Add extra 4ft 2x4 to better support the roof in the front
- Handrails and posts
  - Check with clients with how they would like the stairs, design shown is in the middle
    - If client wants the stairs to either side of the deck you can save a post
- Decking
  - Might want to start with the complex first cut with the 4 posts
    - Support any part of the deck with cleats if needed
- Stairs
  - Do NOT trust the design
  - Remeasure and recalculate on site

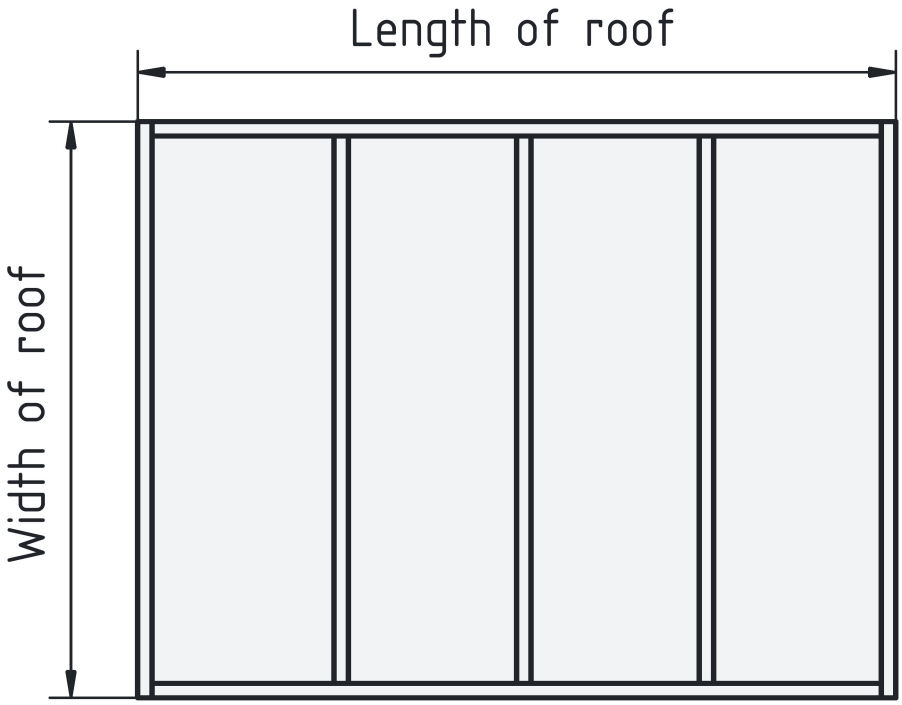



Frame

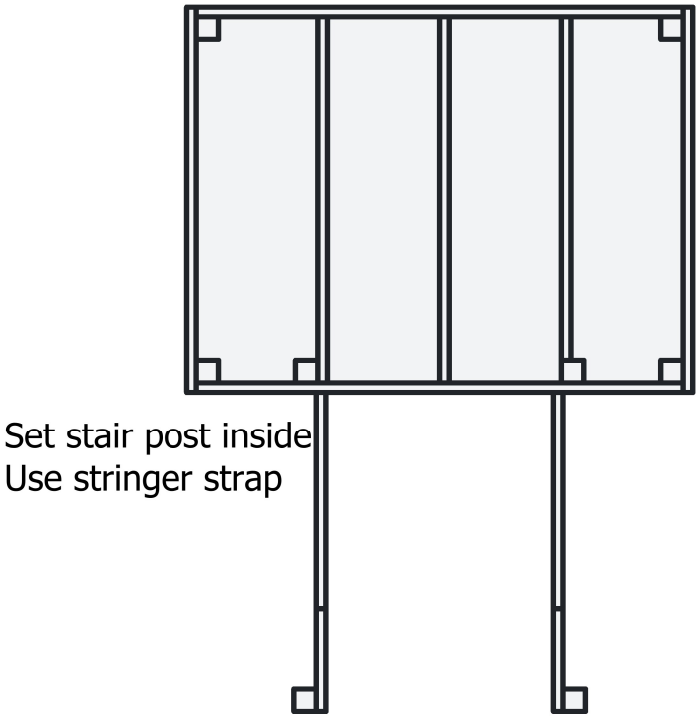

Frame and posts

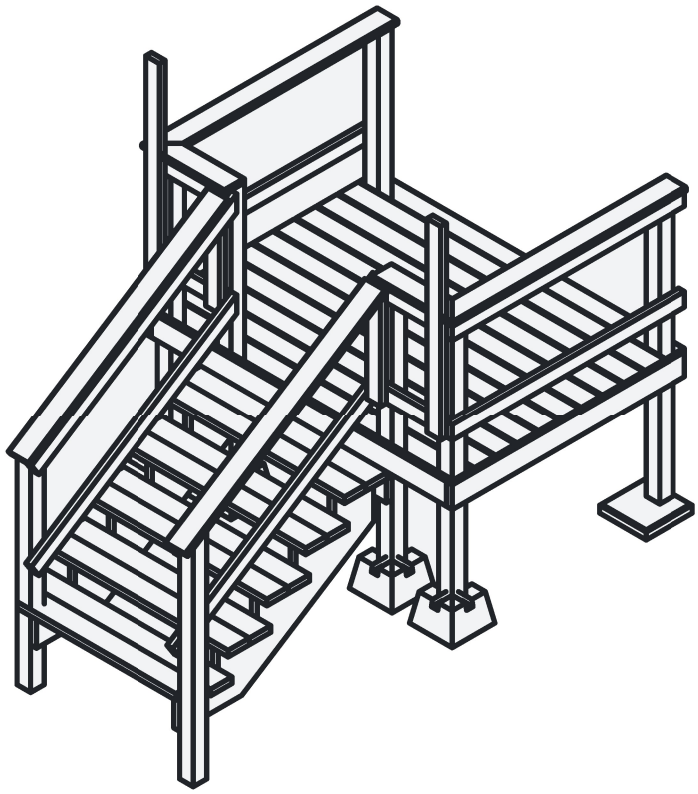

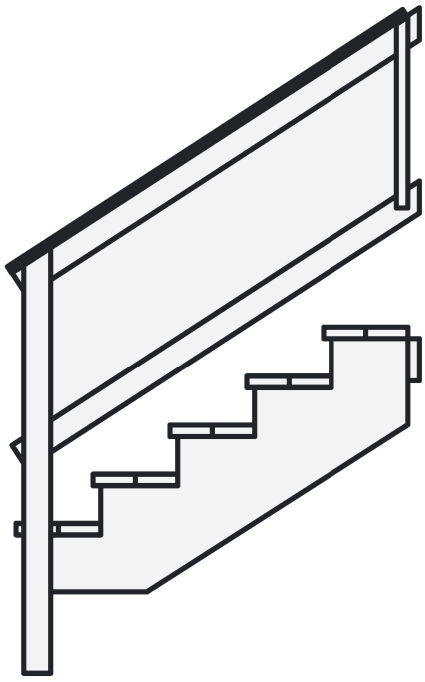

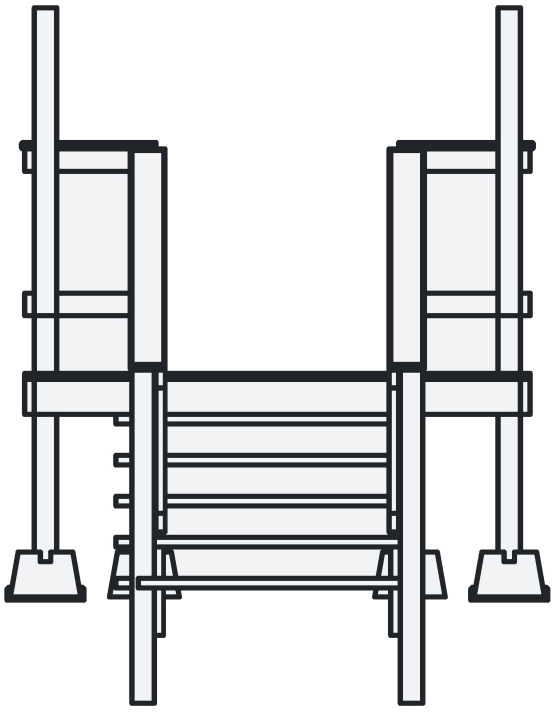

Do NOT use this stair calulation

Materials List

Deck

Item	Amount
Frame	
2x6x8	9
2x6x16	2
4x4x8	6
Pavers	6
Joist Hangers	14
Cleats	
2x6x8	1
2x4x8	2
Handrails	
2x4x8	2
2x4x12	2
Deckboard 10ft	1
Deckboard 16ft	1
Decking	
Deckboard 16ft	18
Special Handrail	
4x4x8	1
2x4x8	2
Red Pavers/ Pavers	8

Total

2x6x8	10
2x6x16	2
4x4x8	7
2x4x8	6
2x4x12	2
Deckboard 10ft	1
Deckboard 16ft	19
Pavers	6
Red Pavers/ Pavers	8
Joist Hangers	14
